I-5/SR-134 CONGESTION MANAGEMENT PROJECT: CONSTRUCTION SCHEDULE
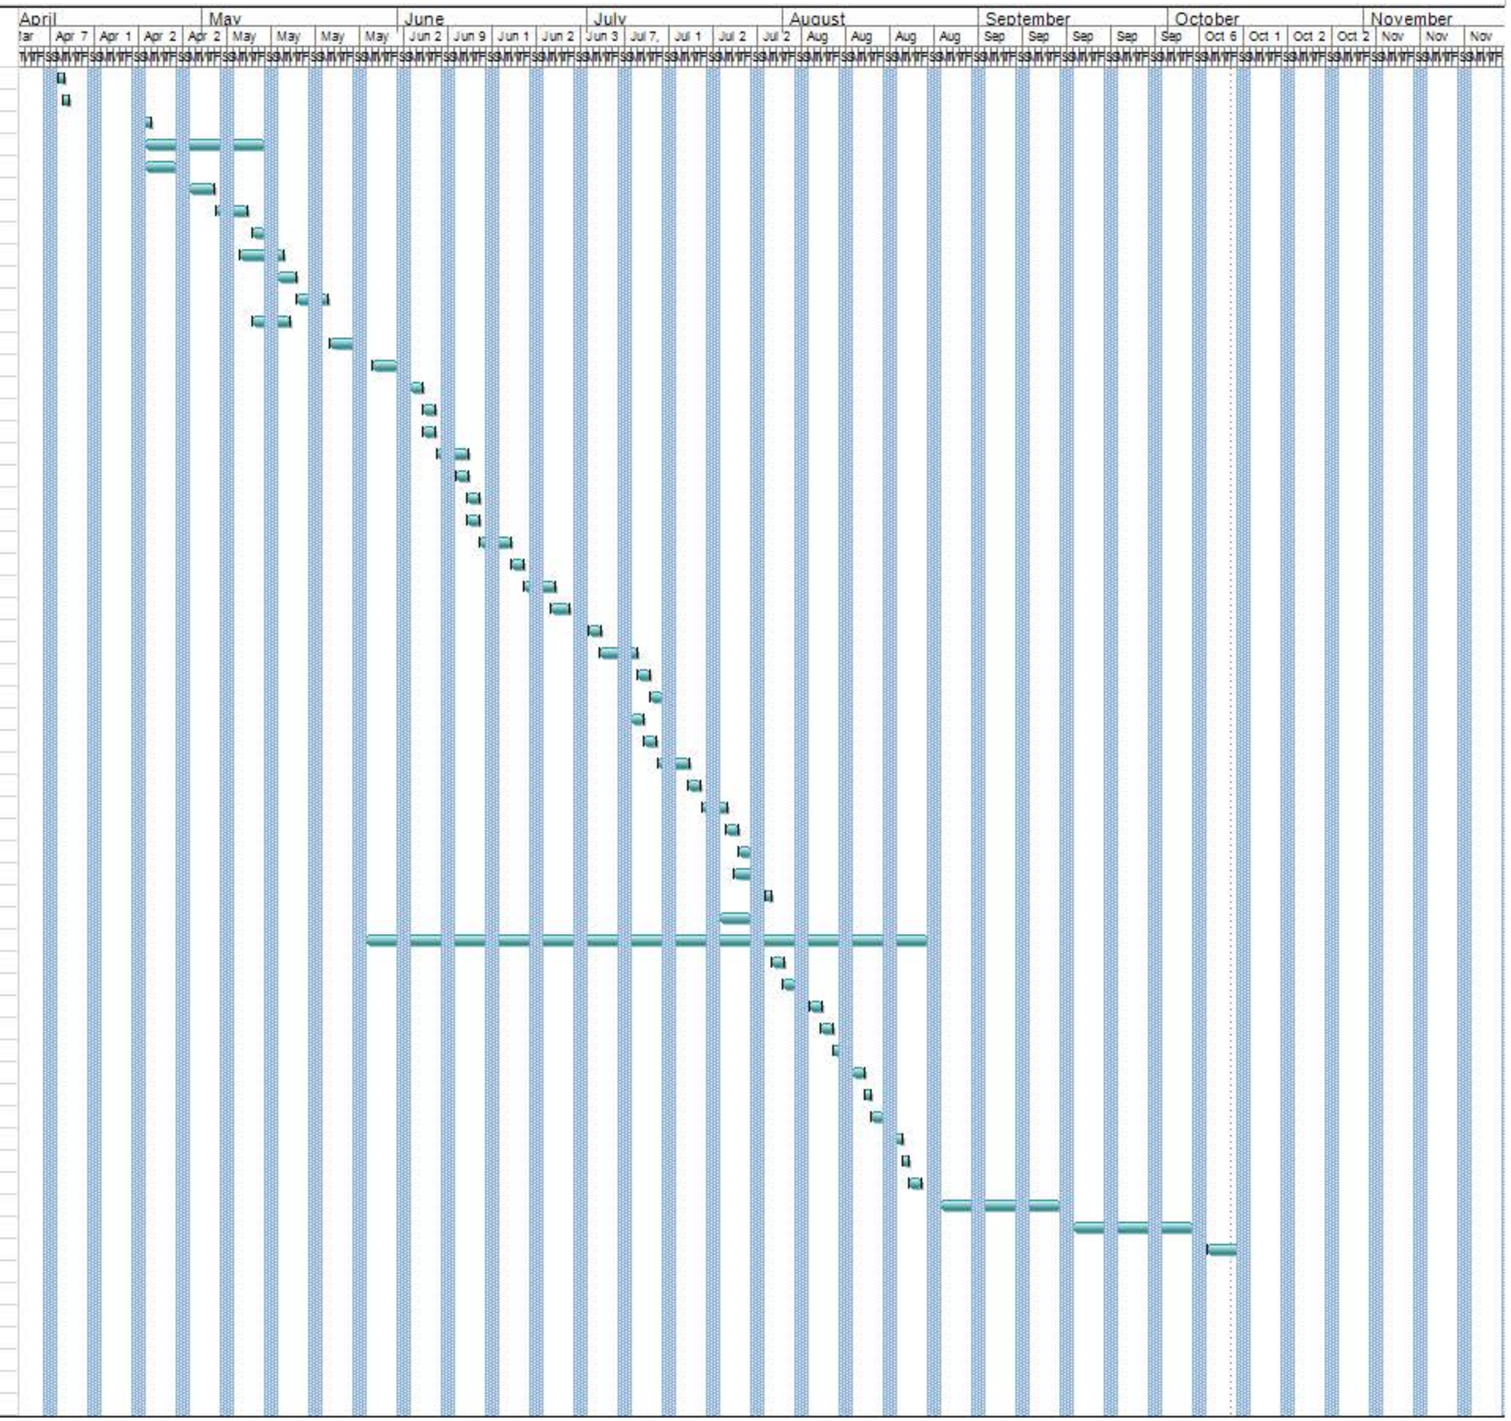
	Task Name	Duration	Start	Finish
1	Award Of Contract	1 day	Mon 4/8/1	Mon 4/8/1
2	Pre Construction Meeting	1 day	Tue 4/9/13	Tue 4/9/13
3	Notice To Proceed	1 day	Mon 4/22/	Mon 4/22/
4	Submittal Review	15 days	Mon 4/22/	Fri 5/10/13
5	Distribute Flyers (first location)	5 days	Mon 4/22/	Fri 4/26/13
6	Locate Utilities @ Sonora & Lake	4 days	Mon 4/29/	Thu 5/2/13
7	Locate Utilities @ Sonora & Flower	3 days	Fri 5/3/13	Tue 5/7/13
8	Locate Utilities @ Riverside & Western	2 days	Thu 5/9/13	Fri 5/10/13
9	Locate Utilities @ Western & Lake	5 days	Tue 5/7/13	Mon 5/13/
10	Install Conduit @ Western & Lake	3 days	Mon 5/13/	Wed 5/15/
11	Install Conduit @ Sonora & Lake	3 days	Thu 5/16/1	Mon 5/20/
12	Locate Utilities @ Sonora & Flower	4 days	Thu 5/9/13	Tue 5/14/1
13	Install Comm Conduit @ Sonora & Flower	4 days	Tue 5/21/1	Fri 5/24/13
14	Install Comm Pull Boxes On Sonora	4 days	Tue 5/28/1	Fri 5/31/13
15	Install Foundations @ Sonora & Lake	2 days	Mon 6/3/1	Tue 6/4/13
16	Terminate Conduit & Set Boxes @ Sonora &	2 days	Wed 6/5/1	Thu 6/6/13
17	Install Foundations @ Western & Lake	2 days	Wed 6/5/1	Thu 6/6/13
18	Terminate Conduit & Set Boxes @ Western	3 days	Fri 6/7/13	Tue 6/11/1
19	Install Traffic Signal Poles @ Sonora & Lake	2 days	Mon 6/10/	Tue 6/11/1
20	Install Cable @ Sonora & Lake	2 days	Wed 6/12/	Thu 6/13/1
21	Install Foundations @ Sonora & Flower	2 days	Wed 6/12/	Thu 6/13/1
22	Terminate Conduit & Set Boxes @ Sonora &	3 days	Fri 6/14/13	Tue 6/18/1
23	Locate Utilities @ Western & Victory	2 days	Wed 6/19/	Thu 6/20/1
24	Locate Utilities @ Victory & Allen	3 days	Fri 6/21/13	Tue 6/25/1
25	Locate Utilities @ Sonora & San Fernando	3 days	Tue 6/25/1	Thu 6/27/1
26	Install Conduit @ Western & Victory	2 days	Mon 7/1/1	Tue 7/2/13
27	Install Conduit @ Victory & Allen	4 days	Wed 7/3/1	Mon 7/8/1
28	Install Conduit @ Sonora & San Fernando	2 days	Tue 7/9/13	Wed 7/10/
29	Install Conduit @ Riverside & Westen	2 days	Thu 7/11/1	Fri 7/12/13
30	Install Foundations @ Western & Victory	2 days	Mon 7/8/1	Tue 7/9/13
31	Terminate Conduit & Set Boxes @ Western	2 days	Wed 7/10/	Thu 7/11/1
32	Install Comm Pull Boxes On Western	3 days	Fri 7/12/13	Tue 7/16/1
33	Install Foundations @ Victory & Allen	2 days	Wed 7/17/	Thu 7/18/1
34	Install Comm Pull Boxes On Victory	2 days	Fri 7/19/13	Mon 7/22/
35	Terminate Conduit & Set Boxes @ Victory &	2 days	Tue 7/23/1	Wed 7/24/
36	Terminate Conduit & Set Boxes @ Riverside	2 days	Thu 7/25/1	Fri 7/26/13
37	Install Controller, Service & Cable @ Sonora	3 days	Wed 7/24/	Fri 7/26/13
38	Install Video Detection @ Sonora & Lake	1 day	Mon 7/29/	Mon 7/29/
39	Install Curb Ramps @ Various Locations	5 days	Mon 7/22/	Fri 7/26/13
40	Restore Sidewalk PCC & Roadway AC	65 days	Mon 5/27/	Fri 8/23/13
41	Install Signal Cable @ Victory & Allen	2 days	Tue 7/30/1	Wed 7/31/
42	Install Signal Cable @ Western & Victory	2 days	Thu 8/1/13	Fri 8/2/13
43	Install Signal Cable @ Western & Lake	2 days	Mon 8/5/1	Tue 8/6/13
44	Install Signal Poles @ Western & Lake	2 days	Wed 8/7/1	Thu 8/8/13
45	Install Video Detection @ Western & Lake	1 day	Fri 8/9/13	Fri 8/9/13
46	Install Signal Poles @ Western & Victory	2 days	Mon 8/12/	Tue 8/13/1
47	Install Video Detection @ Western & Victory	1 day	Wed 8/14/	Wed 8/14/
48	Install Signal Poles @ Victory & Allen	2 days	Thu 8/15/1	Fri 8/16/13
49	Install Video Detection @ Victory & Allen	1 day	Mon 8/19/	Mon 8/19/
50	Install Camera Pole @ Sonora & Flower	1 day	Tue 8/20/1	Tue 8/20/1
51	Install Video Detection @ Sonora & Flower	2 days	Wed 8/21/	Thu 8/22/1
52	Remove Exist Cable & Install New Fiber	15 days	Mon 8/26/	Fri 9/13/13
53	Terminate & Test Fiber Optic Cable	15 days	Mon 9/16/	Fri 10/4/13
54	Punch List & Final Acceptance	5 days	Mon 10/7/	Fri 10/11/1
55		1 day?	Tue 4/9/13	Tue 4/9/13
56		1 day?	Tue 4/9/13	Tue 4/9/13
57		1 day?	Tue 4/9/13	Tue 4/9/13
58		1 day?	Tue 4/9/13	Tue 4/9/13
59		1 day?	Tue 4/9/13	Tue 4/9/13
60		1 day?	Tue 4/9/13	Tue 4/9/13
61		1 day	Tue 4/9/13	Tue 4/9/13
